

Form A2-3: Compliance Verification Report for Inverter Connected Power Generating Modules

This form should be used by the **Manufacturer** to demonstrate and declare compliance with the requirements of EREC G99. The form can be used in a variety of ways as detailed below:

1. To obtain Fully Type Tested status

The **Manufacturer** can use this form to obtain **Fully Type Tested** status for a **Power Generating Module** by registering this completed form with the Energy Networks Association (ENA) Type Test Verification Report Register.

2. To obtain Type Tested status for a product

This form can be used by the **Manufacturer** to obtain **Type Tested** status for a product which is used in a **Power Generating Module** by registering this form with the relevant parts completed with the Energy Networks Association (ENA) Type Test Verification Report Register.

3. One-off Installation

This form can be used by the **Manufacturer** or **Installer** to confirm that the **Power Generating Module** has been tested to satisfy all or part of the requirements of this EREC G99. This form must be submitted to the **DNO** as part of the application.

A combination of (2) and (3) can be used as required, together with Form A2-4 where compliance of the **Interface Protection** is to be demonstrated on site.

Note:

Within this Form A2-3 the term **Power Park Module** will be used but its meaning can be interpreted within Form A2-3 to mean **Power Park Module, Generating Unit or Inverter** as appropriate for the context. However, note that compliance must be demonstrated at the **Power Park Module** level.

If the **Power Generating Module** is **Fully Type Tested** and registered with the Energy Networks Association (ENA) Type Test Verification Report Register, the Installation Document (Form A3) should include the **Manufacturer's** reference number (the Product ID), and this form does not need to be submitted.

Where the **Power Generating Module** is not registered with the ENA Type Test Verification Report Register or is not **Fully Type Tested** this form (all or in parts as applicable) needs to be completed and provided to the **DNO**, to confirm that the **Power Generating Module** has been tested to satisfy all or part of the requirements of this EREC G99.

| | | | |
|---------------------|--------------------------|---|-------------------|
| PGM technology | | Growatt 11000TL3-S, Growatt 12000TL3, Growatt 12000TL3-S, Growatt 13000TL3-S, Growatt 15000TL3-S | |
| Manufacturer name | | Growatt New Energy Technology Co., Ltd. | |
| Address | | 1st East & 3rd Floor of Building A, Building B, Jiayu Industrial Park, #28, GuangHui Road, LongTeng Community, Shiyan Street, Baoan, District, Shenzhen, P.R.China | |
| Tel | +86 755 2951 5888 | Web site | www.ginverter.com |
| E:mail | yunzhong.cai@growatt.com | | |
| Registered Capacity | | 15kW | |

Engineering Recommendation G99 Form A2-3

Type A Power Generating Modules



There are four options for Testing: (1) **Fully Type Tested**, (2) **Partially Type Tested**, (3) one-off installation, (4) tested on site at time of commissioning. The check box below indicates which tests in this Form have been completed for each of the options. With the exception of **Fully Type Tested PGMs** tests marked with * may be carried out at the time of commissioning (Form A4).

| Tested option: | 1. Fully Type Tested | 2. Partially Type Tested | 3. One-off Man. Info. | 4. Tested on Site at time of Commissioning |
|---|-----------------------------|---------------------------------|------------------------------|---|
| 0. Fully Type Tested - all tests detailed below completed and evidence attached to this submission | | N/A | N/A | N/A |
| 1. Operating Range | N/A | | | |
| 2. PQ – Harmonics | | | | |
| 3. PQ – Voltage Fluctuation and Flicker | | | | |
| 4. PQ – DC Injection (Power Park Modules only) | | | | |
| 5. Power Factor (PF)* | | | | |
| 6. Frequency protection trip and ride through tests* | | | | |
| 7. Voltage protection trip and ride through tests* | | | | |
| 8. Protection – Loss of Mains Test*, Vector Shift and RoCoF Stability Test* | | | | |
| 9. LFSM-O Test* | | | | |
| 10. Protection – Reconnection Timer* | | | | |
| 11. Fault Level Contribution | | | | |
| 12. Self-monitoring Solid State Switch | | | | |
| 13. Wiring functional tests if required by para 15.2.1 (attach relevant schedule of tests)* | | | | |
| 14. Logic Interface (input port)* | | | | |

* may be carried out at the time of commissioning (Form A.2-4).


Document reference(s) for **Manufacturers' Information**:

Engineering Recommendation G99 Form A2-3

Type A Power Generating Modules



Manufacturer compliance declaration. - I certify that all products supplied by the company with the above **Type Tested Manufacturer's** reference number will be manufactured and tested to ensure that they perform as stated in this document, prior to shipment to site and that no site **Modifications** are required to ensure that the product meets all the requirements of EREC G99.

| | | | |
|--------|---|--------------|---|
| Signed |  | On behalf of | Growatt New Energy Technology Co., Ltd. |
|--------|---|--------------|---|

Note that testing can be done by the **Manufacturer** of an individual component or by an external test house.

Where parts of the testing are carried out by persons or organisations other than the **Manufacturer** then that person or organisation shall keep copies of all test records and results supplied to them to verify that the testing has been carried out by people with sufficient technical competency to carry out the tests.

A2-3 Compliance Verification Report –Tests for Type A Inverter Connected Power Generating Modules – test record

1. Operating Range: Two tests should be carried with the **Power Generating Module** operating at **Registered Capacity** and connected to a suitable test supply or grid simulation set. The power supplied by the primary source shall be kept stable within $\pm 5\%$ of the apparent power value set for the entire duration of each test sequence.

Frequency, voltage and **Active Power** measurements at the output terminals of the **Power Generating Module** shall be recorded every second. The tests will verify that the **Power Generating Module** can operate within the required ranges for the specified period of time.


The **Interface Protection** shall be disabled during the tests.

In case of a PV **Power Park Module** the PV primary source may be replaced by a DC source.

In case of a full converter **Power Park Module** (eg wind) the primary source and the prime mover **Inverter/rectifier** may be replaced by a DC source.


Test 1

Voltage = 85% of nominal (195.5 V),
 Frequency = 47 Hz,
Power Factor = 1,
 Period of test 20 s

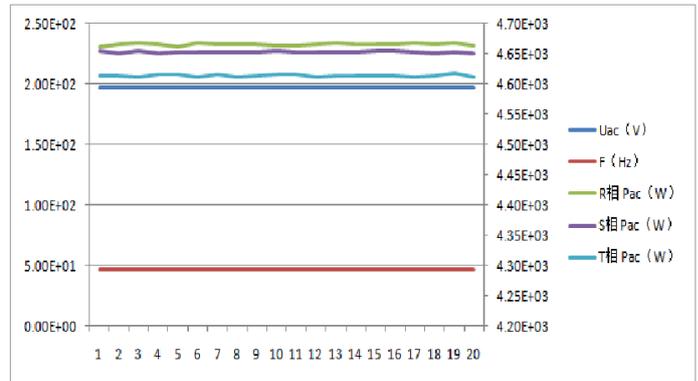

Test 2

Voltage = 85% of nominal (195.5 V),
 Frequency = 47.5 Hz,
Power Factor = 1,
 Period of test 90 minutes

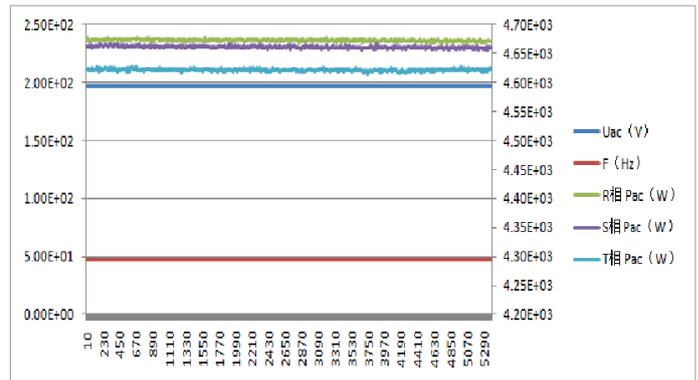

| | |
|--|--|
| <p>Test 3</p> <p>Voltage = 110% of nominal (253 V), Frequency = 51.5 Hz, Power Factor = 1, Period of test 90 minutes</p> | |
| <p>Test 4</p> <p>Voltage = 110% of nominal (253 V), Frequency = 52.0 Hz, Power Factor = 1, Period of test 15 minutes</p> | |

2. Power Quality – Harmonics:

For **Power Generating Modules** of **Registered Capacity** of less than 75 A per phase (ie 50 kW) the test requirements are specified in Annex A.7.1.5. These tests should be carried out as specified in BS EN 61000-3-12 The results need to comply with the limits of Table 2 of BS EN 61000-3-12 for single phase equipment and Table 3 of BS EN 61000-3-12 for three phase equipment.

Power Generating Modules with emissions close to the limits laid down in BS EN 61000-3-12 may require the installation of a transformer between 2 and 4 times the rating of the **Power Generating Module** in order to accept the connection to a **Distribution Network**.

For **Power Generating Modules** of **Registered Capacity** of greater than 75 A per phase (ie 50 kW) the installation must be designed in accordance with EREC G5.

| Power Generating Module tested to BS EN 61000-3-12 | | | | | | |
|--|----------------------------------|-------|-----------------------------|-------|---------------------------|---|
| Power Generating Module rating per phase (rpp) | | 5 | | kVA | | Harmonic % = Measured Value (A) x 23/rating per phase (kVA) |
| Harmonic | At 45-55% of Registered Capacity | | 100% of Registered Capacity | | Limit in BS EN 61000-3-12 | |
| | Measured Value MV in Amps | % | Measured Value MV in Amps | % | 1 phase | 3 phase |
| 2 | 0.1788 | 0.209 | 0.1825 | 0.540 | 8% | 8% |
| 3 | 0.0361 | 1.024 | 0.2068 | 0.093 | 21.6% | Not stated |

Engineering Recommendation G99 Form A2-3

Type A Power Generating Modules

| | | | | | | |
|-------------------|--------|-------|--------|-------|-------|------------|
| 4 | 0.2241 | 0.174 | 0.0844 | 1.283 | 4% | 4% |
| 5 | 0.3280 | 1.652 | 0.0062 | 2.042 | 10.7% | 10.7% |
| 6 | 0.0117 | 0.090 | 0.0208 | 0.053 | 2.67% | 2.67% |
| 7 | 0.2000 | 1.204 | 0.0470 | 1.166 | 7.2% | 7.2% |
| 8 | 0.0861 | 0.015 | 0.0072 | 0.534 | 2% | 2% |
| 9 | 0.0070 | 0.057 | 0.0313 | 0.060 | 3.8% | Not stated |
| 10 | 0.0202 | 0.038 | 0.0223 | 0.10. | 1.6% | 1.6% |
| 11 | 0.0474 | 0.652 | 0.0813 | 0.281 | 3.1% | 3.1% |
| 12 | 0.0065 | 0.051 | 0.0057 | 0.034 | 1.33% | 1.33% |
| 13 | 0.0324 | 0.057 | 0.0384 | 0.190 | 2% | 2% |
| THD ¹ | | | 1.803 | | 23% | 13% |
| PWHD ² | | | 1.817 | | 23% | 22% |

¹ THD = Total Harmonic Distortion

² PWHD = Partial Weighted Harmonic Distortion

Engineering Recommendation G99 Form A2-3

Type A Power Generating Modules



| Power Generating Module tested to BS EN 61000-3-12 | | | | | | |
|---|---|-------|------------------------------------|-------|---|------------|
| Power Generating Module rating per phase (rpp) | | | 5 | kVA | Harmonic % = Measured Value (A) x 23/rating per phase (kVA) | |
| Harmonic | At 45-55% of Registered Capacity | | 100% of Registered Capacity | | Limit in BS EN 61000-3-12 | |
| | Measured Value MV in Amps | % | Measured Value MV in Amps | % | 1 phase | 3 phase |
| 2 | 0.0922 | 0.248 | 0.1000 | 1.178 | 8% | 8% |
| 3 | 0.0158 | 0.848 | 0.0157 | 0.090 | 21.6% | Not stated |
| 4 | 0.2190 | 0.248 | 0.2257 | 1.383 | 4% | 4% |
| 5 | 0.4945 | 1.231 | 0.5101 | 1.958 | 10.7% | 10.7% |
| 6 | 0.0088 | 0.103 | 0.0083 | 0.051 | 2.67% | 2.67% |
| 7 | 0.3183 | 1.025 | 0.3098 | 1.202 | 7.2% | 7.2% |
| 8 | 0.0900 | 0.065 | 0.0964 | 0.491 | 2% | 2% |
| 9 | 0.0056 | 0.053 | 0.0101 | 0.036 | 3.8% | Not stated |
| 10 | 0.0236 | 0.049 | 0.0213 | 0.121 | 1.6% | 1.6% |
| 11 | 0.0480 | 0.444 | 0.0828 | 0.273 | 3.1% | 3.1% |
| 12 | 0.0058 | 0.016 | 0.0062 | 0.042 | 1.33% | 1.33% |
| 13 | 0.0323 | 0.356 | 0.0408 | 0.182 | 2% | 2% |
| THD ³ | | | 1.75 | | 23% | 13% |
| PWHD ⁴ | | | 1.761 | | 23% | 22% |
| Power Generating Module tested to BS EN 61000-3-12 | | | | | | |
| Power Generating Module rating per phase (rpp) | | | 5 | kVA | Harmonic % = Measured Value (A) x 23/rating per phase (kVA) | |
| Harmonic | At 45-55% of Registered Capacity | | 100% of Registered Capacity | | Limit in BS EN 61000-3-12 | |
| | Measured Value MV in Amps | % | Measured Value MV in Amps | % | 1 phase | 3 phase |

³ THD = Total Harmonic Distortion

⁴ PWHD = Partial Weighted Harmonic Distortion

| | | | | | | |
|-------------------|--------|-------|--------|-------|-------|------------|
| 2 | 0.2025 | 0.325 | 0.2209 | 0.828 | 8% | 8% |
| 3 | 0.0154 | 1.203 | 0.0122 | 0.046 | 21.6% | Not stated |
| 4 | 0.2379 | 0.379 | 0.2417 | 0.906 | 4% | 4% |
| 5 | 0.3367 | 1.029 | 0.4945 | 1.854 | 10.7% | 10.7% |
| 6 | 0.0088 | 0.089 | 0.0088 | 0.033 | 2.67% | 2.67% |
| 7 | 0.2068 | 1.043 | 0.3183 | 1.193 | 7.2% | 7.2% |
| 8 | 0.0844 | 0.041 | 0.0828 | 0.337 | 2% | 2% |
| 9 | 0.0062 | 0.055 | 0.0062 | 0.021 | 3.8% | Not stated |
| 10 | 0.0208 | 0.067 | 0.0408 | 0.089 | 1.6% | 1.6% |
| 11 | 0.0470 | 0.426 | 0.0820 | 0.307 | 3.1% | 3.1% |
| 12 | 0.0072 | 0.022 | 0.0075 | 0.028 | 1.33% | 1.33% |
| 13 | 0.0313 | 0.378 | 0.0403 | 0.151 | 2% | 2% |
| THD ⁵ | | | 1.75 | | 23% | 13% |
| PWHD ⁶ | | | 1.75 | | 23% | 22% |

3. Power Quality – Voltage fluctuations and Flicker:

For **Power Generating Modules of Registered Capacity** of less than 75 A per phase (ie 50 kW) these tests should be undertaken in accordance with Annex A.7.1.4.3. Results should be normalised to a standard source impedance, or if this results in figures above the limits set in BS EN 61000-3-11 to a suitable Maximum Impedance.

For **Power Generating Modules of Registered Capacity** of greater than 75 A per phase (ie 50 kW) the installation must be designed in accordance with EREC P28.

| | Starting | | | Stopping | | | Running | |
|-----------------------------------|----------|------|------|----------|------|------|---------|--------------|
| | d max | d c | d(t) | d max | d c | d(t) | P st | P It 2 hours |
| Measured Values at test impedance | 0.169 | 0.24 | 0 | 0.169 | 0.24 | 0 | 0.042 | 0.040 |
| Normalised to standard | 0.169 | 0.24 | 0 | 0.169 | 0.24 | 0 | 0.042 | 0.040 |

⁵ THD = Total Harmonic Distortion

⁶ PWHD = Partial Weighted Harmonic Distortion

| | | | | | | | | |
|---|----------------------|-----------------|----------|---------------|------------------|------|------|----------|
| impedance | | | | | | | | |
| Normalised to required maximum impedance | - | - | - | - | - | - | - | - |
| Limits set under BS EN 61000-3-11 | 4% | 3.3% | 3.3% | 4% | 3.3% | 3.3% | 1.0 | 0.65 |
| | | | | | | | | |
| Test Impedance | R | 0.24 | Ω | XI | 0.15 | | | Ω |
| Standard Impedance | R | 0.24 * 0.4 ^ | Ω | XI | 0.15 * 0.25 ^ | | | Ω |
| Maximum Impedance | R | - | Ω | XI | - | | | Ω |
| <p>* Applies to three phase and split single phase Power Generating Modules.</p> <p>^ Applies to single phase Power Generating Module and Power Generating Modules using two phases on a three phase system</p> <p>For voltage change and flicker measurements the following formula is to be used to convert the measured values to the normalised values where the Power Factor of the generation output is 0.98 or above.</p> <p>Normalised value = Measured value x reference source resistance/measured source resistance at test point</p> <p>Single phase units reference source resistance is 0.4 Ω</p> <p>Two phase units in a three phase system reference source resistance is 0.4 Ω</p> <p>Two phase units in a split phase system reference source resistance is 0.24 Ω</p> <p>Three phase units reference source resistance is 0.24 Ω</p> <p>Where the Power Factor of the output is under 0.98 then the XI to R ratio of the test impedance should be close to that of the Standard Impedance.</p> <p>The stopping test should be a trip from full load operation.</p> <p>The duration of these tests need to comply with the particular requirements set out in the testing notes for the technology under test. Dates and location of the test need to be noted below</p> | | | | | | | | |
| Test start date | 22.JAN.2019 | | | Test end date | 23.JAN.2019 | | | |
| Test location | Growatt R&D Test Lab | | | | | | | |
| <p>4. Power quality – DC injection: The tests should be carried out on a single Generating Unit. Tests are to be carried out at three defined power levels $\pm 5\%$. At 230 V a 50 kW three phase Inverter has a current output of 217 A so DC limit is 543 mA. These tests should be undertaken in accordance with Annex A.7.1.4.4.</p> | | | | | | | | |
| Test power level | 10% | | | 55% | | | 100% | |

| | | | |
|--------------------------|--------------------|----------------------|--------------------|
| Recorded value in Amps | 17mA/16.5mA/17.1mA | 21.5mA/22.1mA/21.3mA | 12.1mA/11.8mA/12mA |
| as % of rated AC current | 0.08%/0.08%/0.08% | 0.09%/0.09%/0.09% | 0.05%/0.05%/0.05% |
| Limit | 0.25% | 0.25% | 0.25% |

5. Power Factor: The tests should be carried out on a single **Power Generating Module**. Tests are to be carried out at three voltage levels and at **Registered Capacity**. Voltage to be maintained within $\pm 1.5\%$ of the stated level during the test. These tests should be undertaken in accordance with Annex A.7.1.4.2.

| | | | |
|---------------------------|-------------------|-------------------|-------------------|
| Voltage | 0.94 pu (216.2 V) | 1 pu (230 V) | 1.1 pu (253 V) |
| Measured value | 0.998/0.997/0.998 | 0.998/0.998/0.999 | 0.998/0.998/0.998 |
| Power Factor Limit | >0.95 | >0.95 | >0.95 |

6. Protection – Frequency tests: These tests should be carried out in accordance with the Annex A.7.1.2.3.

| Function | Setting | | Trip test | | “No trip tests” | |
|-------------|-----------|------------|-----------|------------|--------------------|-----------------|
| | Frequency | Time delay | Frequency | Time delay | Frequency /time | Confirm no trip |
| U/F stage 1 | 47.5 Hz | 20 s | 47.49Hz | 20.19s | 47.7 Hz 25 s | No trip |
| U/F stage 2 | 47 Hz | 0.5 s | 46.99Hz | 0.661s | 47.2 Hz 19.98 s | No trip |
| | | | | | 46.8 Hz 0.48 s | No trip |
| O/F | 52 Hz | 0.5 s | 52.01Hz | 0.555s | 51.8 Hz 89.98 s | No trip |
| | | | | | 52.2 Hz 0.48 s | No trip |

Note. For frequency trip tests the frequency required to trip is the setting ± 0.1 Hz. In order to measure the time delay a larger deviation than the minimum required to operate the protection can be used. The “No trip tests” need to be carried out at the setting ± 0.2 Hz and for the relevant times as shown in the table above to ensure that the protection will not trip in error.

7. Protection – Voltage tests: These tests should be carried out in accordance with Annex A.7.1.2.2.

| Function | Setting | | Trip test | | “No trip tests” | |
|----------|---------|------------|-----------|------------|-----------------|-----------------|
| | Voltage | Time delay | Voltage | Time delay | Voltage /time | Confirm no trip |
| U/V | 0.8 pu | 2.5 s | 183V | 2.503s | 188 V | No trip |

| | | | | | | |
|-------------|----------------------|-------|------|--------|-------------------|---------|
| | (184 V) | | | | 3.50 s | |
| | | | | | 180 V 2.48 s | No trip |
| O/V stage 1 | 1.14 pu (262.2 V) | 1.0 s | 263V | 1.001s | 258.2 V 2.0 s | No trip |
| O/V stage 2 | 1.19 pu (273.7 V) | 0.5 s | 274V | 0.513s | 269.7 V 0.98s | No trip |
| | | | | | 277.7 V 0.48 s | No trip |

Note for Voltage tests the Voltage required to trip is the setting ± 3.45 V. The time delay can be measured at a larger deviation than the minimum required to operate the protection. The No trip tests need to be carried out at the setting ± 4 V and for the relevant times as shown in the table above to ensure that the protection will not trip in error.

8. Protection – Loss of Mains test: These tests should be carried out in accordance with BS EN 62116. Annex A.7.1.2.4.

The following sub set of tests should be recorded in the following table.

| Test Power and imbalance | 33% -5% Q Test 22 | 66% -5% Q Test 12 | 100% -5% P Test 5 | 33% +5% Q Test 31 | 66% +5% Q Test 21 | 100% +5% P Test 10 |
|-----------------------------|-------------------------|-------------------------|-------------------------|-------------------------|-------------------------|--------------------------|
| Trip time. Limit is 0.5s | 0.294 | 0.367 | 0.353 | 0.298 | 0.347 | 0.390 |

| Loss of Mains Protection, Vector Shift Stability test. This test should be carried out in accordance with Annex A.7.1.2.6. | | | | |
|--|------------------------------|---------------|----------------------|-----------------------|
| | Start Frequency | Change | Confirm no trip | |
| Positive Vector Shift | 49.5 Hz | +50 degrees | No trip | |
| Negative Vector Shift | 50.5 Hz | - 50 degrees | No trip | |
| Loss of Mains Protection, RoCoF Stability test: This test should be carried out in accordance with Annex A.7.1.2.6. | | | | |
| Ramp range | Test frequency ramp: | Test Duration | Confirm no trip | |
| 49.0 Hz to 51.0 Hz | +0.95 Hzs ⁻¹ | 2.1 s | No trip | |
| 51.0 Hz to 49.0 Hz | -0.95 Hzs ⁻¹ | 2.1 s | No trip | |
| 9. Limited Frequency Sensitive Mode – Over frequency test: The test should be carried out using the specific threshold frequency of 50.4 Hz and Droop of 10%. This test should be carried out in accordance with Annex A.7.1.3. | | | | |
| Active Power response to rising frequency/time plots are attached if frequency injection tests are undertaken in accordance with Annex A.7.2.4. | | | Y/N | |
| Alternatively, simulation results should be noted below: | | | | |
| Test sequence at Registered Capacity >80% | Measured Active Power Output | Frequency | Primary Power Source | Active Power Gradient |
| Step a) 50.00Hz ±0.01Hz | 15003.2W | 50Hz | 15350.5W | - |
| Step b) 50.45Hz ±0.05Hz | 14752.7W | 50.449Hz | | - |
| Step c) 50.70Hz ±0.10Hz | 13606.9W | 50.7Hz | | - |
| Step d) 51.15Hz ±0.05Hz | 11702.8W | 51.15Hz | | - |
| Step e) 50.70Hz ±0.10Hz | 13575.3W | 50.7Hz | | - |
| Step f) 50.45Hz ±0.05Hz | 13377.8W | 50.45Hz | | - |

| | | | | |
|---|-------------------------------------|-----------|----------------------|------------------------------|
| Step g) 50.00Hz ±0.01Hz | 15036.6W | 49.999Hz | | |
| Test sequence at Registered Capacity 40% - 60% | Measured Active Power Output | Frequency | Primary Power Source | Active Power Gradient |
| Step a) 50.00Hz ±0.01Hz | 7325.83W | 50HzHz | 7488.56W | - |
| Step b) 50.45Hz ±0.05Hz | 7229.8W | 50.45Hz | | - |
| Step c) 50.70Hz ±0.10Hz | 6636.25W | 50.699Hz | | - |
| Step d) 51.15Hz ±0.05Hz | 5740.14W | 51.149Hz | | - |
| Step e) 50.70Hz ±0.10Hz | 6655.15W | 50.7Hz | | - |

10. Protection – Re-connection timer.

Test should prove that the reconnection sequence starts after a minimum delay of 20 s for restoration of voltage and frequency to within the stage 1 settings of Table 10.1.

| | | | | | |
|---|----------------|--|----------------------|------------|------------|
| Time delay setting | Measured delay | Checks on no reconnection when voltage or frequency is brought to just outside stage 1 limits of Table 10.1. | | | |
| 60 | 60 | At 1.16 pu (266.2 V) | At 0.85 pu (196.1 V) | At 47.4 Hz | At 52.1 Hz |
| Confirmation that the Power Generating Module does not re-connect. | | Yes | Yes | Yes | Yes |

11. Fault level contribution: These tests shall be carried out in accordance with EREC G99 Annex A.7.1.5.

For **Inverter** output

| | | |
|------------------|-------|------------|
| Time after fault | Volts | Amps |
| 20ms | 10V | 0.4A |
| 100ms | 9.2V | 0.31 |
| 250ms | 8.7V | 0.22 |
| 500ms | 8.3V | 0.18 |
| Time to trip | 0.15 | In seconds |

| | |
|---|----------|
| 12. Self-Monitoring solid state switching: No specified test requirements. Refer to Annex A.7.1.7. | |
| It has been verified that in the event of the solid state switching device failing to disconnect the Power Park Module , the voltage on the output side of the switching device is reduced to a value below 50 volts within 0.5 s. | Yes/ NA |
| 13. Wiring functional tests: If required by para 15.2.1. | |
| Confirm that the relevant test schedule is attached (tests to be undertaken at time of commissioning) | Yes / NA |
| 14. Logic interface (input port). | |
| Confirm that an input port is provided and can be used to shut down the module. | Yes / NA |
| Additional comments. | |
| | |
